



Data Date: 08/12/2022


Progress Against Day 1 Requirements

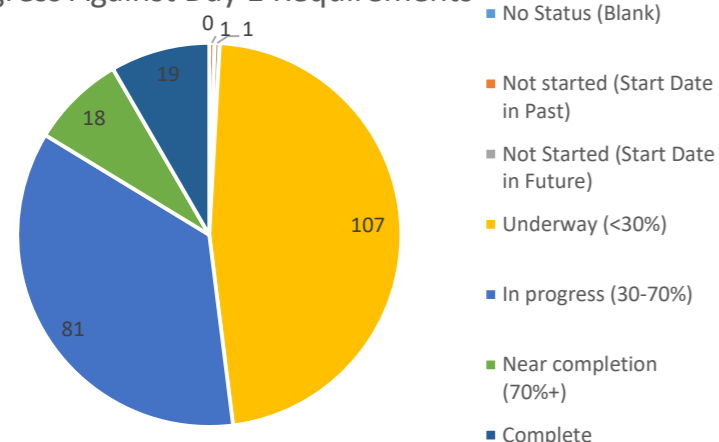

Breakdown by Theme

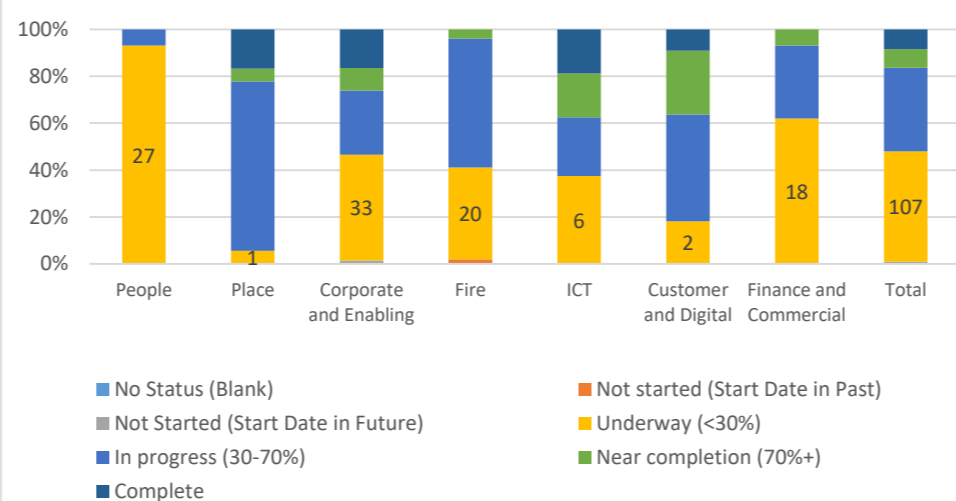

Requirements and Milestones that are incomplete and due, flagged or upcoming

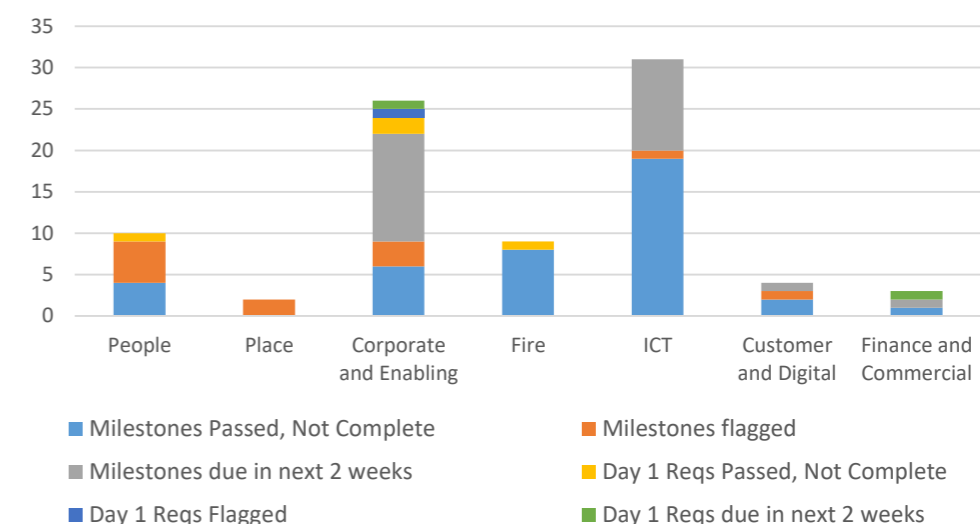

Day 1 requirements and milestone count

	People	Place	Corporate and Enabling	Fire	ICT	Customer and Digital	Finance and Commercial	Total
Day 1 requirements	29	18	73	51	16	11	29	227
L1 milestones	-	-	47	-	18	4	4	73
↳ Or Fire Board	-	-	-	40	-	-	-	40
L2 milestones	14	7	64	21	125	10	3	244
L3 milestones	83	69	230	31	442	33	72	960
	97	76	341	92	585	47	79	1317

Day 1 requirements status updates

	People	Place	Corporate and Enabling	Fire	ICT	Customer and Digital	Finance and Commercial	Total
No Status (Blank)	0	0	0	0	0	0	0	0
Not started (Start Date in Past)	0	0	0	1	0	0	0	1
Not Started (Start Date in Future)	0	0	1	0	0	0	0	1
Underway (<30%)	27	1	33	20	6	2	18	107
In progress (30-70%)	2	13	20	28	4	5	9	81
Near completion (70%+)	0	1	7	2	3	3	2	18
Complete	0	3	12	0	3	1	0	19
	29	18	73	51	16	11	29	227

Milestone & Day 1 Requirements Summary

	People	Place	Corporate and Enabling	Fire	ICT	Customer and Digital	Finance and Commercial	Total
Milestones Complete	39	13	185	9	179	24	26	475
Milestones Complete (%)	40.2%	17.1%	54.3%	9.8%	30.6%	51.1%	32.9%	36.1%
Milestones Passed, Not Complete	4	0	6	8	19	2	1	40
Milestones flagged	5	2	3	0	1	1	0	12
Milestones due in next 2 weeks	0	0	13	0	11	1	1	26
Day 1 Reqs Passed, Not Complete	1	0	2	1	0	0	0	4
Day 1 Reqs Flagged	0	0	1	0	0	0	0	1
Day 1 Reqs due in next 2 weeks	0	0	1	0	0	0	1	2

Actions snapshot

<p>The Delivery plans include 4698 lines of data, of which:</p> <ul style="list-style-type: none"> 93.3% have an owner 90.3% have a start date 91.4% have an end date 93.5% have a status recorded 	<p>Of data marked as a Day 1 Requirement or a Milestone:</p> <ul style="list-style-type: none"> 100.0% have an owner 100.0% have a start date 100.0% have an end date 100.0% have a status recorded
----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------	-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------
